

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predecessor
1	Kick Off Meeting intro to Appirio	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
2	Provide Training Plan	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
3	Analysis&Training document	61 days	0%	Late	Fri 7/26/13	Fri 10/18/13	
4	System Admin Online Training 32 Courses	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
5	Rick	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
6	Dawn	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
7	Sheila	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
8	Josh	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
9	Antonio	60 days	0%	Late	Fri 7/26/13	Thu 10/17/13	
10	TNT Training	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
11	Genett	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
12	TNT	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
13	TNT	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
14	TNT8	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
15	TNT9	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
16	TNT 10	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
17	TNT 11	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
18	TNT 12	30 days	0%	Late	Mon 9/9/13	Fri 10/18/13	
19	Design	74 days?	31%	Late	Tue 8/27/13	Fri 12/6/13	
20	Design Communication and Training Strategy	1 day?	0%	Late	Tue 10/1/13	Tue 10/1/13	
21	Build Training Strategy	1 day?	0%	Late	Tue 10/1/13	Tue 10/1/13	
22	Single Sign On (John and Brian)	23 days?	53%	Late	Mon 10/7/13	Wed 11/6/13	
23	Provide name ID in assertion for login info	3 days	100%	Complete	Mon 10/7/13	Wed 10/9/13	
24	Test using various users	5 days	100%	Complete	Thu 10/10/13	Wed 10/16/13	23
25	Validate if assertion and certification in pilot will be the same in production	1 day?	100%	Complete	Wed 10/23/13	Wed 10/23/13	
26	Approve to move to Live	1 day?	100%	Complete	Thu 10/24/13	Thu 10/24/13	25
27	Move to Live	9 days	0%	Late	Fri 10/25/13	Wed 11/6/13	26
28	Virtual Training WebEX	25 days?	18%	Late	Thu 10/10/13	Wed 11/13/13	
29	Provide credentials	1 day?	100%	Complete	Thu 10/10/13	Thu 10/10/13	
30	Validate credential-build in pilot	1 day?	100%	Complete	Thu 10/17/13	Thu 10/17/13	29
31	Execute test cases provided by Nubia	5 days	0%	Late	Fri 11/1/13	Thu 11/7/13	30
32	Move to Production	4 days	0%	Future Task	Fri 11/8/13	Wed 11/13/13	31
33	Custom Log In Page	22 days?	100%	Complete	Mon 9/30/13	Tue 10/29/13	
38	Inbound Data Feed - Need to automate files to FTP *Nubia is settir	16 days?	6%	Late	Thu 10/10/13	Thu 10/31/13	
39	Put in request to automate files	1 day?	100%	Complete	Thu 10/31/13	Thu 10/31/13	
40	Confirm automation is in place	10 days	0%	Late	Thu 10/10/13	Wed 10/23/13	

Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predecessor
41	Test inbound data	3 days	0%	Late	Thu 10/24/13	Mon 10/28/13	40
42	Approve to move to live	1 day?	0%	Late	Tue 10/29/13	Tue 10/29/13	41
43	Move to live	1 day?	0%	Late	Wed 10/30/13	Wed 10/30/13	42
44	Outbound Data Feed (EDM)	21 days?	39%	Late	Fri 9/27/13	Fri 10/25/13	
45	Complete design documents	8 days	100%	Complete	Fri 9/27/13	Tue 10/8/13	
46	Provide sample data to load into Pilot	1 day?	100%	Complete	Wed 10/9/13	Wed 10/9/13	45
47	Validate with CSOD	9 days	0%	Late	Thu 10/10/13	Tue 10/22/13	46
48	test from CSOD FTP to SMUD	2 days	0%	Late	Wed 10/23/13	Thu 10/24/13	47
49	test SMUD file to EDM	1 day?	0%	Late	Fri 10/25/13	Fri 10/25/13	48
50	approve to move to LIVE	1 day?	0%	Late	Fri 10/25/13	Fri 10/25/13	
51	Move to LIVE or close project	1 day?	0%	Late	Fri 10/25/13	Fri 10/25/13	
52	Historical Data Load	23 days?	65%	Late	Wed 10/9/13	Fri 11/8/13	
53	Provide sample data	6 days?	100%	Complete	Wed 10/9/13	Wed 10/16/13	
54	Edit data (separate classroom vs. on line)	5 days	100%	Complete	Thu 10/17/13	Wed 10/23/13	53
55	Provide upload to Nubia	4 days	100%	Complete	Thu 10/24/13	Tue 10/29/13	54
56	Nubia to advise that new upload is good to go	1 day?	0%	Late	Wed 10/30/13	Wed 10/30/13	55
57	Test new upload	5 days	0%	Late	Thu 10/31/13	Wed 11/6/13	56
58	Approve to move to Live	2 days	0%	Future Task	Thu 11/7/13	Fri 11/8/13	57
59	Master Data Load	37 days?	39%	Late	Tue 10/1/13	Wed 11/20/13	
60	Identify process for SCORM only content-Media PRO	7 days	0%	Late	Mon 10/14/13	Tue 10/22/13	
61	Provide sample of MediaPro to Nubia	2 days	100%	Complete	Wed 10/23/13	Thu 10/24/13	60
62	Build the framework for the NERC and Info. Privacy Prot courses	10 days	0%	Late	Fri 10/25/13	Thu 11/7/13	61
63	Test if results can be uploaded to LMS	5 days	0%	Future Task	Fri 11/8/13	Thu 11/14/13	62
64	Load partial data in PILOT (5)	10 days?	100%	Complete	Tue 10/1/13	Mon 10/14/13	
65	SCORM courses loaded into Pilot	16 days	75%	Late	Tue 10/15/13	Tue 11/5/13	64
66	SCORM links sent to eLearn COP for test	4 days	0%	On Schedule	Wed 11/6/13	Mon 11/11/13	65
67	AICC Courses input and tested - DEFER	1 day?	0%	Future Task	Tue 11/12/13	Tue 11/12/13	66
68	validate can move to LIVE	1 day?	0%	Future Task	Wed 11/13/13	Wed 11/13/13	67
69	Build in LIVE	5 days	0%	Future Task	Thu 11/14/13	Wed 11/20/13	68
70	Web Services	27 days?	4%	Late	Tue 10/1/13	Wed 11/6/13	
71	Identify how Web Services will be use EDM (batch)	18 days?	6%	Late	Tue 10/1/13	Thu 10/24/13	
72	Provide template to Nubia	5 days	0%	Late	Fri 10/25/13	Thu 10/31/13	71
73	Develop Web Services in Pilot	1 day?	0%	Late	Fri 11/1/13	Fri 11/1/13	72
74	Test in Pilot	1 day?	0%	Late	Mon 11/4/13	Mon 11/4/13	73
75	Approve to move to LIVE	1 day?	0%	Late	Tue 11/5/13	Tue 11/5/13	74
76	Move to LIVE	1 day?	0%	On Schedule	Wed 11/6/13	Wed 11/6/13	75
77	Distribution e-mails	24 days?	27%	Late	Mon 10/14/13	Thu 11/14/13	

Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predecessor
78	Configure in the Pilot system	17 days?	32%	Late	Mon 10/14/13	Tue 11/5/13	
79	Build e-mails with standard language	4 days	75%	Late	Mon 10/21/13	Thu 10/24/13	
80	Create Functional Test Cases	2 days	0%	On Schedule	Wed 11/6/13	Thu 11/7/13	
81	Functional testing in Pilot	1 day?	0%	Future Task	Fri 11/8/13	Fri 11/8/13	80
82	Send to Pat K for Brand editing	5 days	0%	On Schedule	Wed 11/6/13	Tue 11/12/13	78
83	Configure / Build in LIVE	2 days	0%	Future Task	Wed 11/13/13	Thu 11/14/13	82
84	Security Roles	67 days?	40%	On Schedule	Tue 8/27/13	Wed 11/27/13	
85	Work with Brandt to complete template/workboo	6 days?	100%	Complete	Mon 10/7/13	Mon 10/14/13	
86	Provide template to Nubia	1 day?	100%	Complete	Mon 10/14/13	Mon 10/14/13	
87	Configure Security Roles	1 day?	100%	Complete	Tue 10/15/13	Tue 10/15/13	86
88	Create Functional Test Cases	3 days	0%	Future Task	Fri 11/8/13	Tue 11/12/13	
89	Test in Pilot	1 day	0%	Late	Tue 8/27/13	Fri 11/15/13	
90	configure Security Roles in Live	8 days	0%	Future Task	Mon 11/18/13	Wed 11/27/13	89
91	Mandatory Training-Corporate GRID	39 days?	2%	Late	Tue 10/15/13	Fri 12/6/13	
92	Determine and document when OU is used or Create Custom Groups	1 day?	50%	Late	Tue 10/15/13	Fri 11/8/13	
93	Determine if we use Curriculum or Certifications	18 days	0%	Late	Wed 10/16/13	Fri 11/8/13	
94	Research if multiple course and multiple curriculum	1 day	100%	Complete	Wed 11/6/13	Wed 11/6/13	
95	Build events (Mandatory Grid)	1 day	0%	Future Task	Fri 11/8/13	Fri 11/8/13	
96	Build on line courses (Mandatory Grid)	1 day	0%	Future Task	Fri 11/8/13	Fri 11/8/13	
97	Build one location for all Mandatory Training e.g. Custom Page	1 day	0%	Future Task	Mon 11/11/13	Mon 11/11/13	96
98	Verify 2014 Courses + Descriptions EVENTS	3 days	0%	On Schedule	Wed 11/6/13	Fri 11/8/13	
99	Verify 2014 Courses + Descriptions ONLINE	3 days?	0%	On Schedule	Wed 11/6/13	Fri 11/8/13	
100	Create Sessions for 2014 Events	1 day?	0%	Future Task	Mon 11/11/13	Mon 11/11/13	98
101	Create Functional Test Cases	3 days	0%	Future Task	Fri 11/8/13	Tue 11/12/13	
102	Create Functional Test Cases	3 days	0%	Future Task	Fri 11/8/13	Tue 11/12/13	
103	Create Functional Test Cases	3 days	0%	Future Task	Fri 11/8/13	Tue 11/12/13	
104	Test Your MT Events, Sessions, Courses & Reports	15 days	0%	Late	Thu 10/24/13	Wed 11/13/13	
105	Complete the training and proxy in as your manager to test if it show	1 day?	0%	Future Task	Wed 11/13/13	Wed 11/13/13	
106	Move to LIVE	1 day?	0%	Future Task	Thu 11/14/13	Thu 11/14/13	105
107	Active Courses	23 days?	0%	Schedule	Wed 11/6/13	Fri 12/6/13	
108	Pull list of active courses into Excel Checklist	2 days	5%	On Schedule	Wed 11/6/13	Thu 11/7/13	
109	Verify Course Descriptions in Pilot for your assigned courses	4 days	0%	Future Task	Fri 11/8/13	Wed 11/13/13	108
110	Move to LIVE	1 day?	0%	Future Task	Thu 11/14/13	Thu 11/14/13	109
111	Use Excel checklist to Complete/Edit Event Data for your assign	5 days	0%	Future Task	Fri 11/15/13	Thu 11/21/13	110
112	Use Excel checklist to Schedule sessions for your course (may	10 days	0%	Future Task	Fri 11/22/13	Thu 12/5/13	111
113	Sign Off in LIVE	1 day?	0%	Future Task	Fri 12/6/13	Fri 12/6/13	112
114	Construction Pilot/Workbook	1 day?	0%	Future Task	Thu 11/14/13	Thu 11/14/13	105

Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predece
115	System Preferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
116	Update WB-Corporate Preferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
117	Update WB-Define Fiscal Year	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
118	Update WB-Display Preferences by Division	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
119	Update WB-Global Search Preferences by Division	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
120	Update WB-LogIn Messages by Division	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
121	Update WB-Manage Custom Pages	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
122	Update WB-Manage On Line providers	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
123	Update WB-Mobil ePreferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
124	Update WB-MyAccount Preferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
125	Update WB-People Finder by Division	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
126	Update WB-Time Zone Preferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
127	Update WB-Welcome Page Preferences	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
128	Configure in Live	10 days	0%	Late	Mon 10/21/13	Fri 11/1/13	
129	Security Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
130	Update WB-Email preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
131	Update WB-IP WhiteList by Divisions	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
132	Update WB-Navigation Tabs and Links	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
133	Update WB-Password Preferences by Division	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
134	Configure in Live	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
135	Connect Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
136	Update WB-Connect Preferences by Division	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
137	Update WB-Posting Type Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
138	Configure in Live	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
139	Learning Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
140	Update WB-Activate Express Training....	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
141	Update WB-Activate Reasons for Training	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
142	Update WB-Activate Session Cancellation	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
143	Update WB-Activate Session Withdrawal..	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
144	Update WB-Configure External Training	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
145	Update WB-Content Launching Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
146	Update WB-Content Requesting Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
147	Update WB-Course Rating Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
148	Update WB-Custom Certificate Defaults	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
149	Update WB-Custom Certificates by Division	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
150	Update WB-Default Approver Reqs.	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
151	Update WB-Default Approver Workflows	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
152	Update WB-Define Custom Fields for training	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
153	Update WB-ILT Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	

Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predecessor
154	Update WB-Search Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
155	Update WB-Set Evaluation Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
156	Update WB-Subject Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
157	Update WB-Training Completion Signature	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
158	Update WB-Training Reason Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
159	Update WB-Transcript Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
160	Update WB-My Team Talent Profile	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
161	SAVE WORK BOOK UNDER LEARNING CENTER	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
162	Configure in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
163	Report Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
164	Update WB-Report Delivery Preferences	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
165	Configure in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
166	Test & Approve in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
167	Single Sign On	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
168	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
169	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
170	Virtual Training WebEX	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
171	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
172	Validate in LVIE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
173	Custom Log In Page	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
174	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
175	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
176	Outbound Data Feed (EDM) Nubia waiting for her tech team *need	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
177	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
178	Validate in Live	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
179	Historical Data Load	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
180	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
181	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
182	Master Data Load	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
183	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
184	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
185	Web Services	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
186	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
187	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
188	Distribution e-mails	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
189	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
190	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	


Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Percent complete	Status	Start	Finish	Predecessor
191	Security Roles	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
192	Update workboo	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
193	Validate in LIVE	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
194	Certifications	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
195	COPY DOWN TO PILOT	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
196	If cut off date is used for HDL, then we another upload from CSOD - keep p	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
197	Training needs to be added to the schedule	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
198	Post support	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
199	DEFERRED WORK	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	
200	AICC courses	1 day?	0%	Late	Fri 7/26/13	Fri 7/26/13	

Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

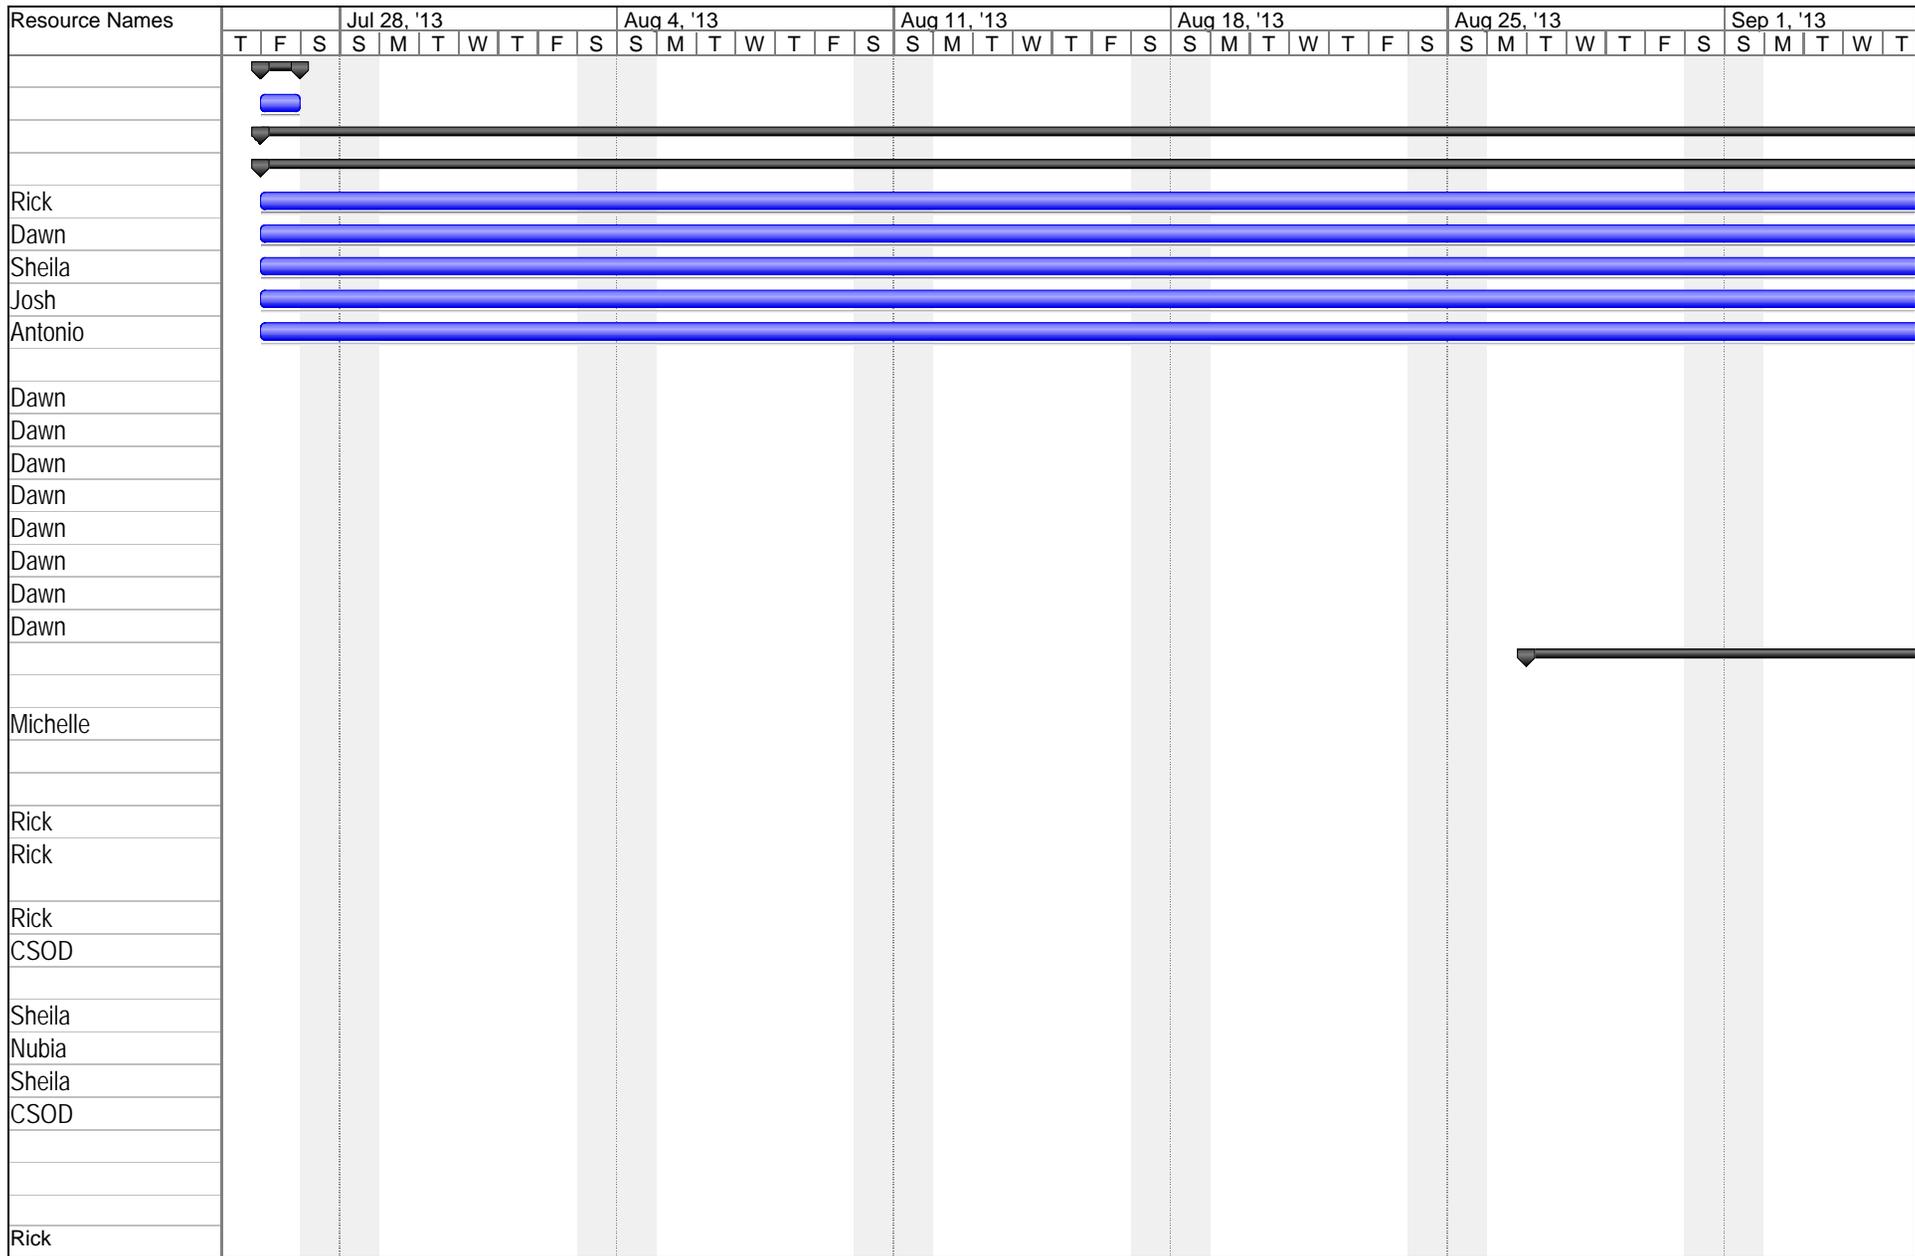


Project: LMS Project schedule as of 11/6/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Resource Names	Jul 28, '13			Aug 4, '13			Aug 11, '13			Aug 18, '13			Aug 25, '13			Sep 1, '13														
	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
Josh/ Lori																														
Nubia																														
Josh																														
Team																														
Josh																														
Josh																														
Sheila																														
Sheila																														
Dawn																														
Dawn																														
Team																														
Dawn or Sheila																														
Rick																														
Krishna/ Rick/ Sheila																														
Rick																														
Sheila																														
Dawn																														
Dawn																														
Lori,Jennie																														
Lori,Jennie																														
Lori / Laura																														
Antoinio																														
Gennette																														
Steve																														
Team																														
Team																														
Dawn/Sheila/Rick																														
Dawn & Rick																														
Team																														
CSOD?																														
Team																														
Team																														
Team																														




Project: LMS Project schedule as of 10/1/13 Date: Wed 11/6/13	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

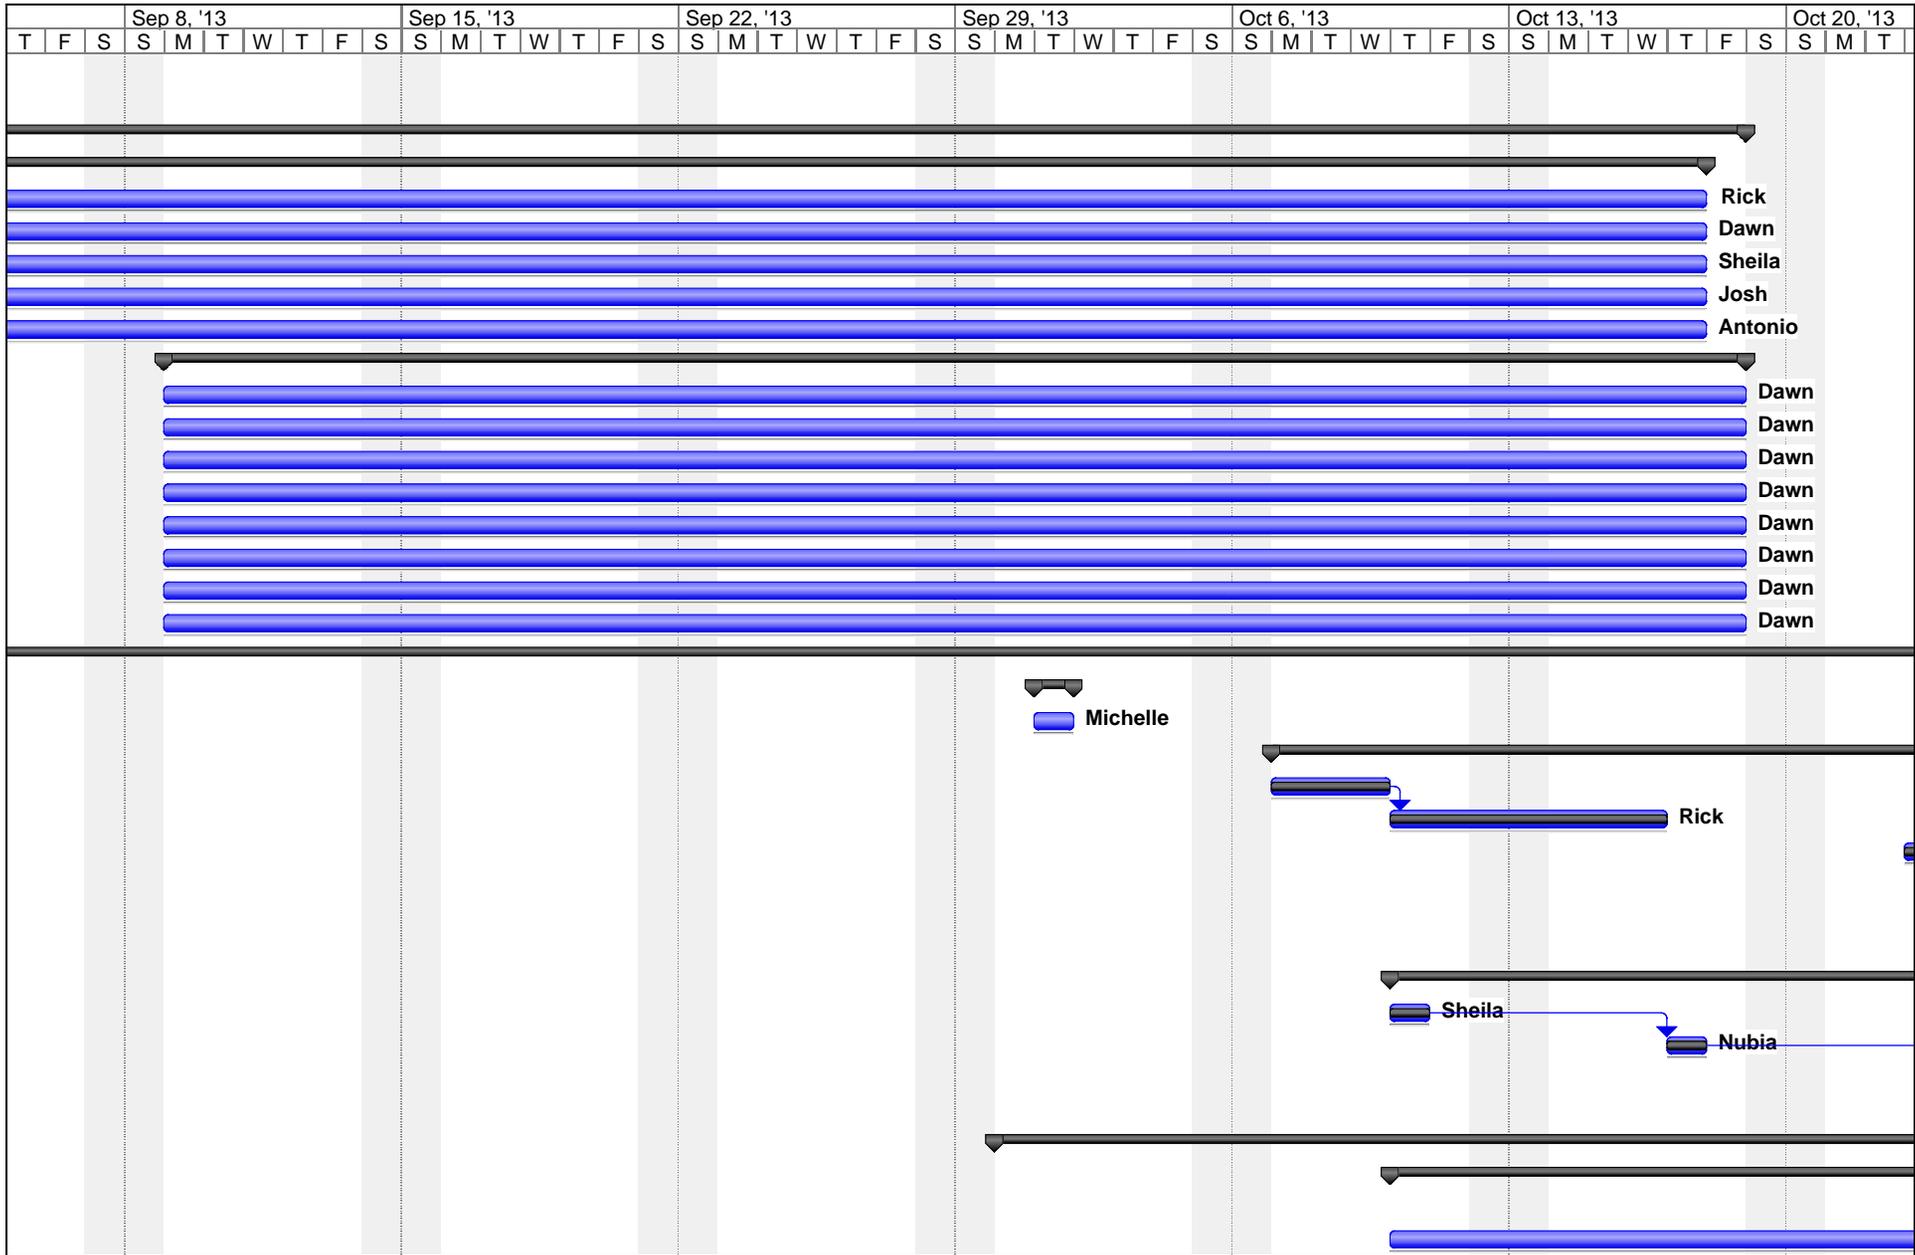


Project: LMS Project schedule as of 10/11/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

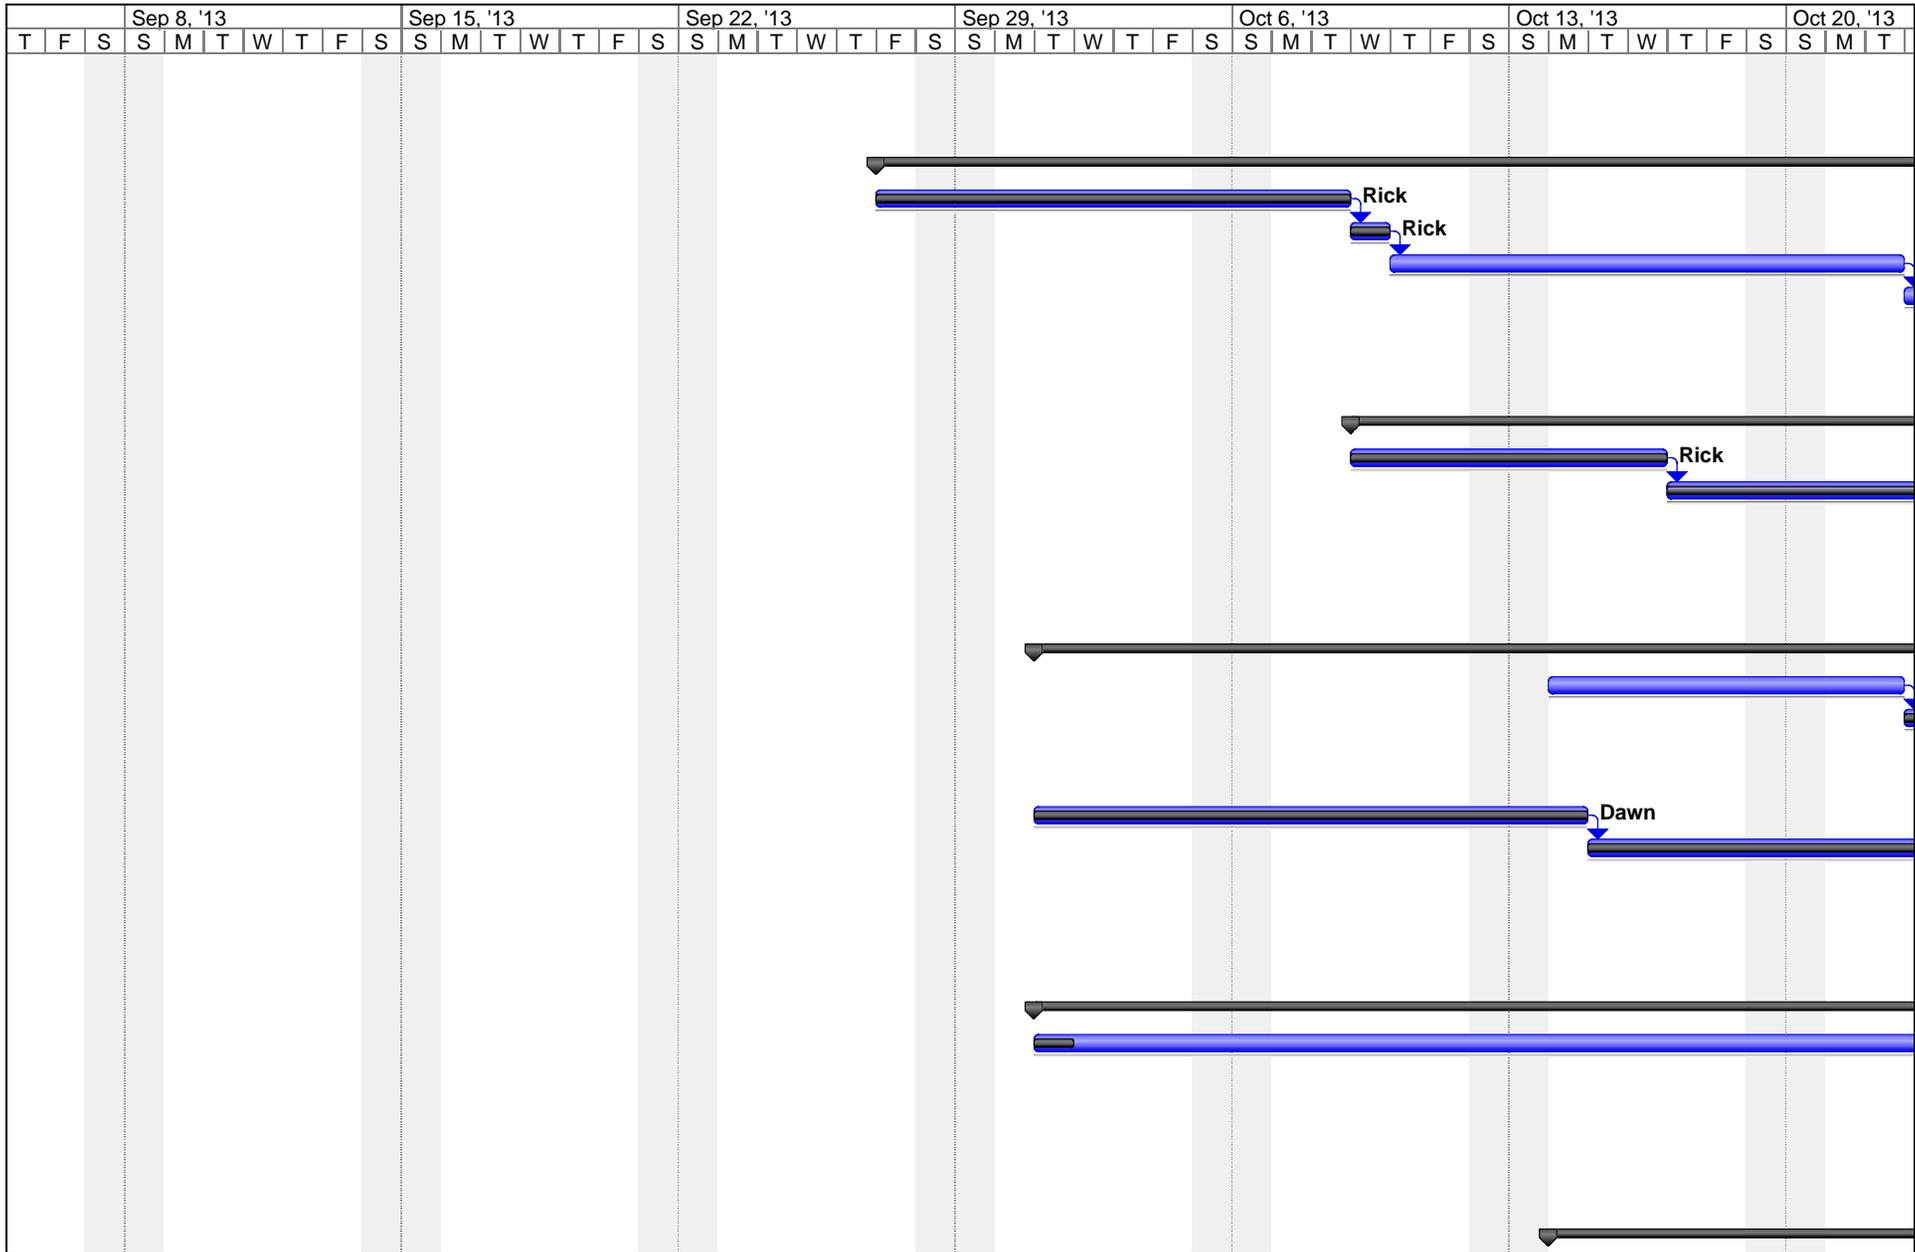


Project: LMS Project schedule as of 10/11/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

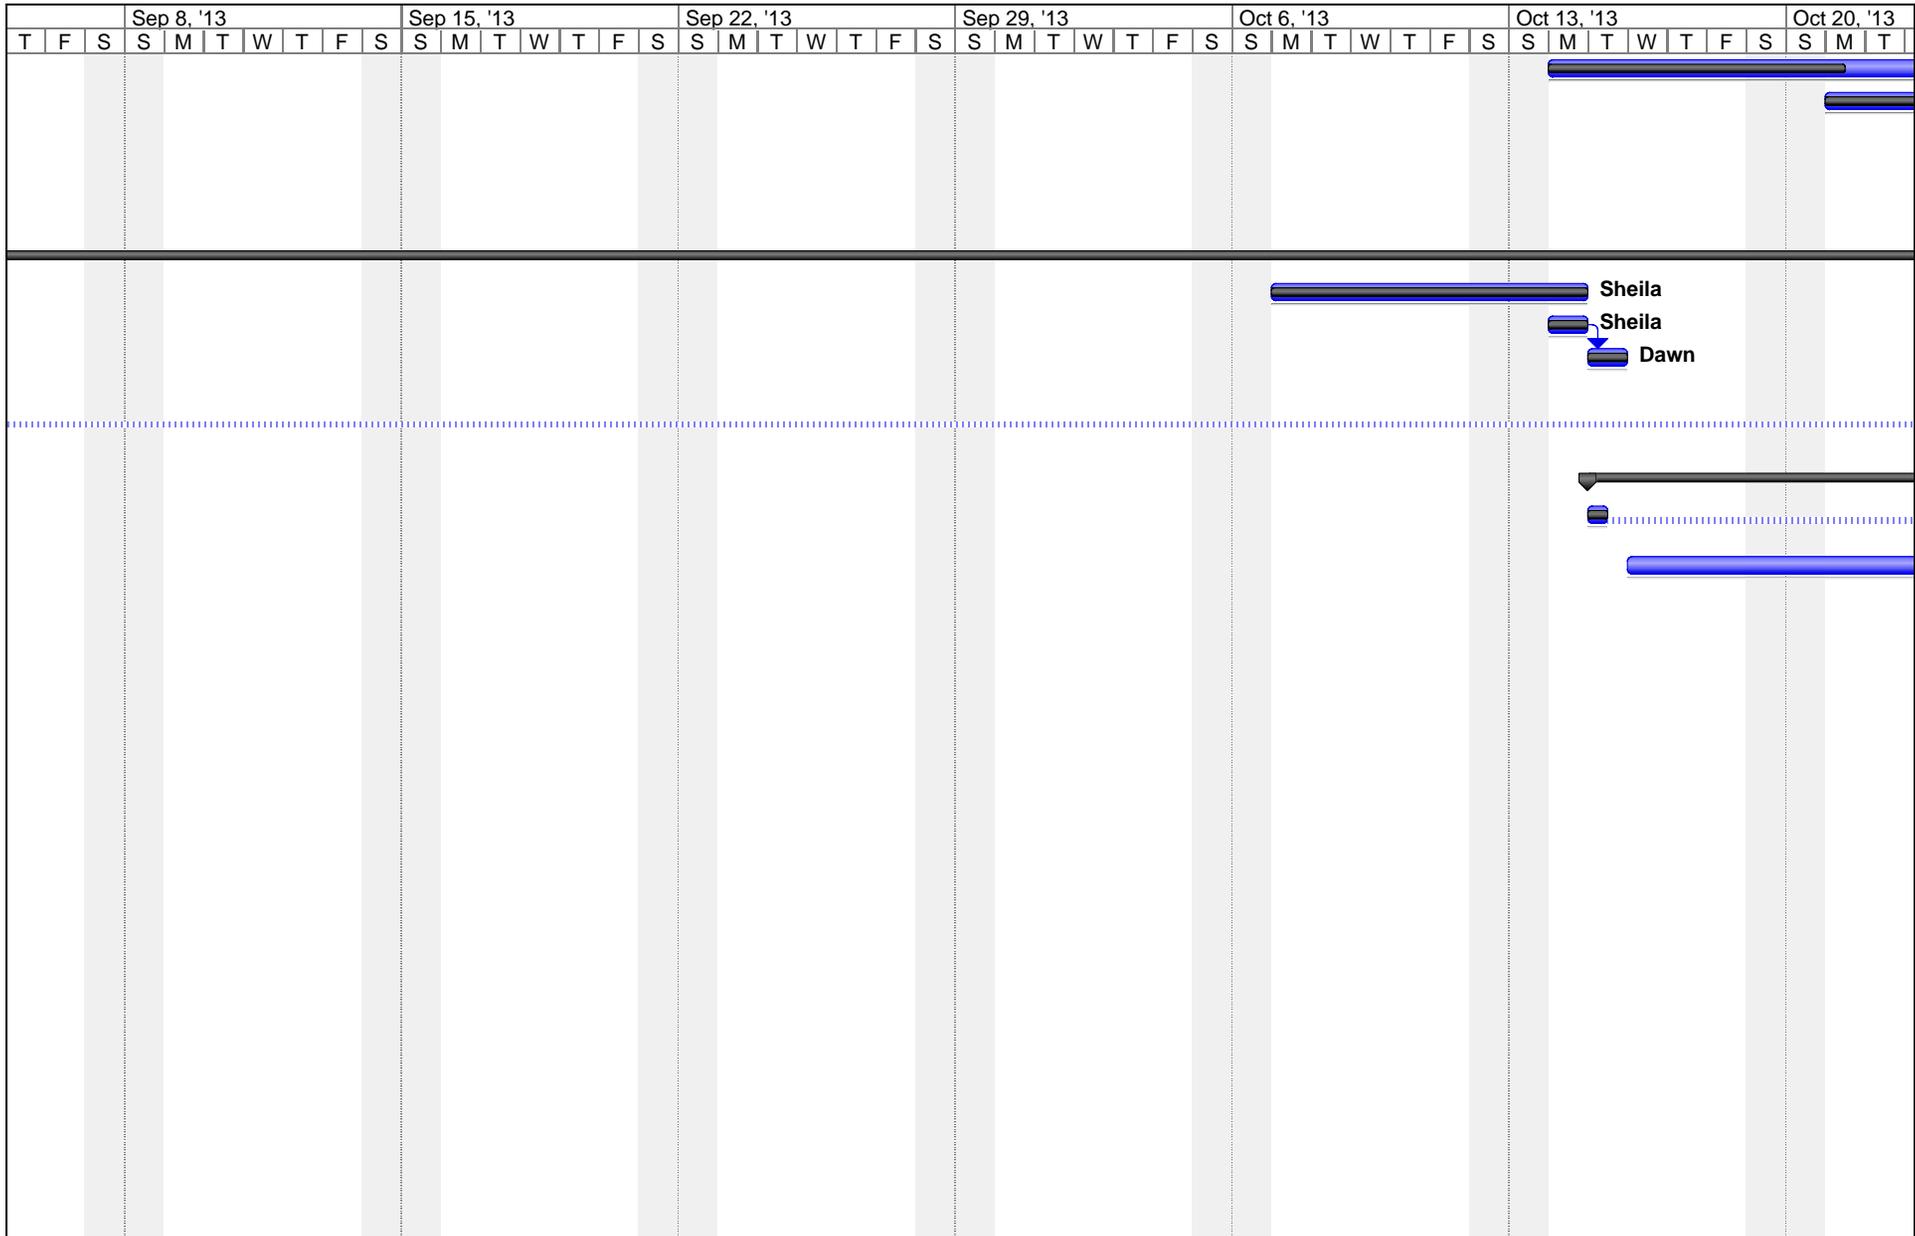


Project: LMS Project schedule as of 11/6/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

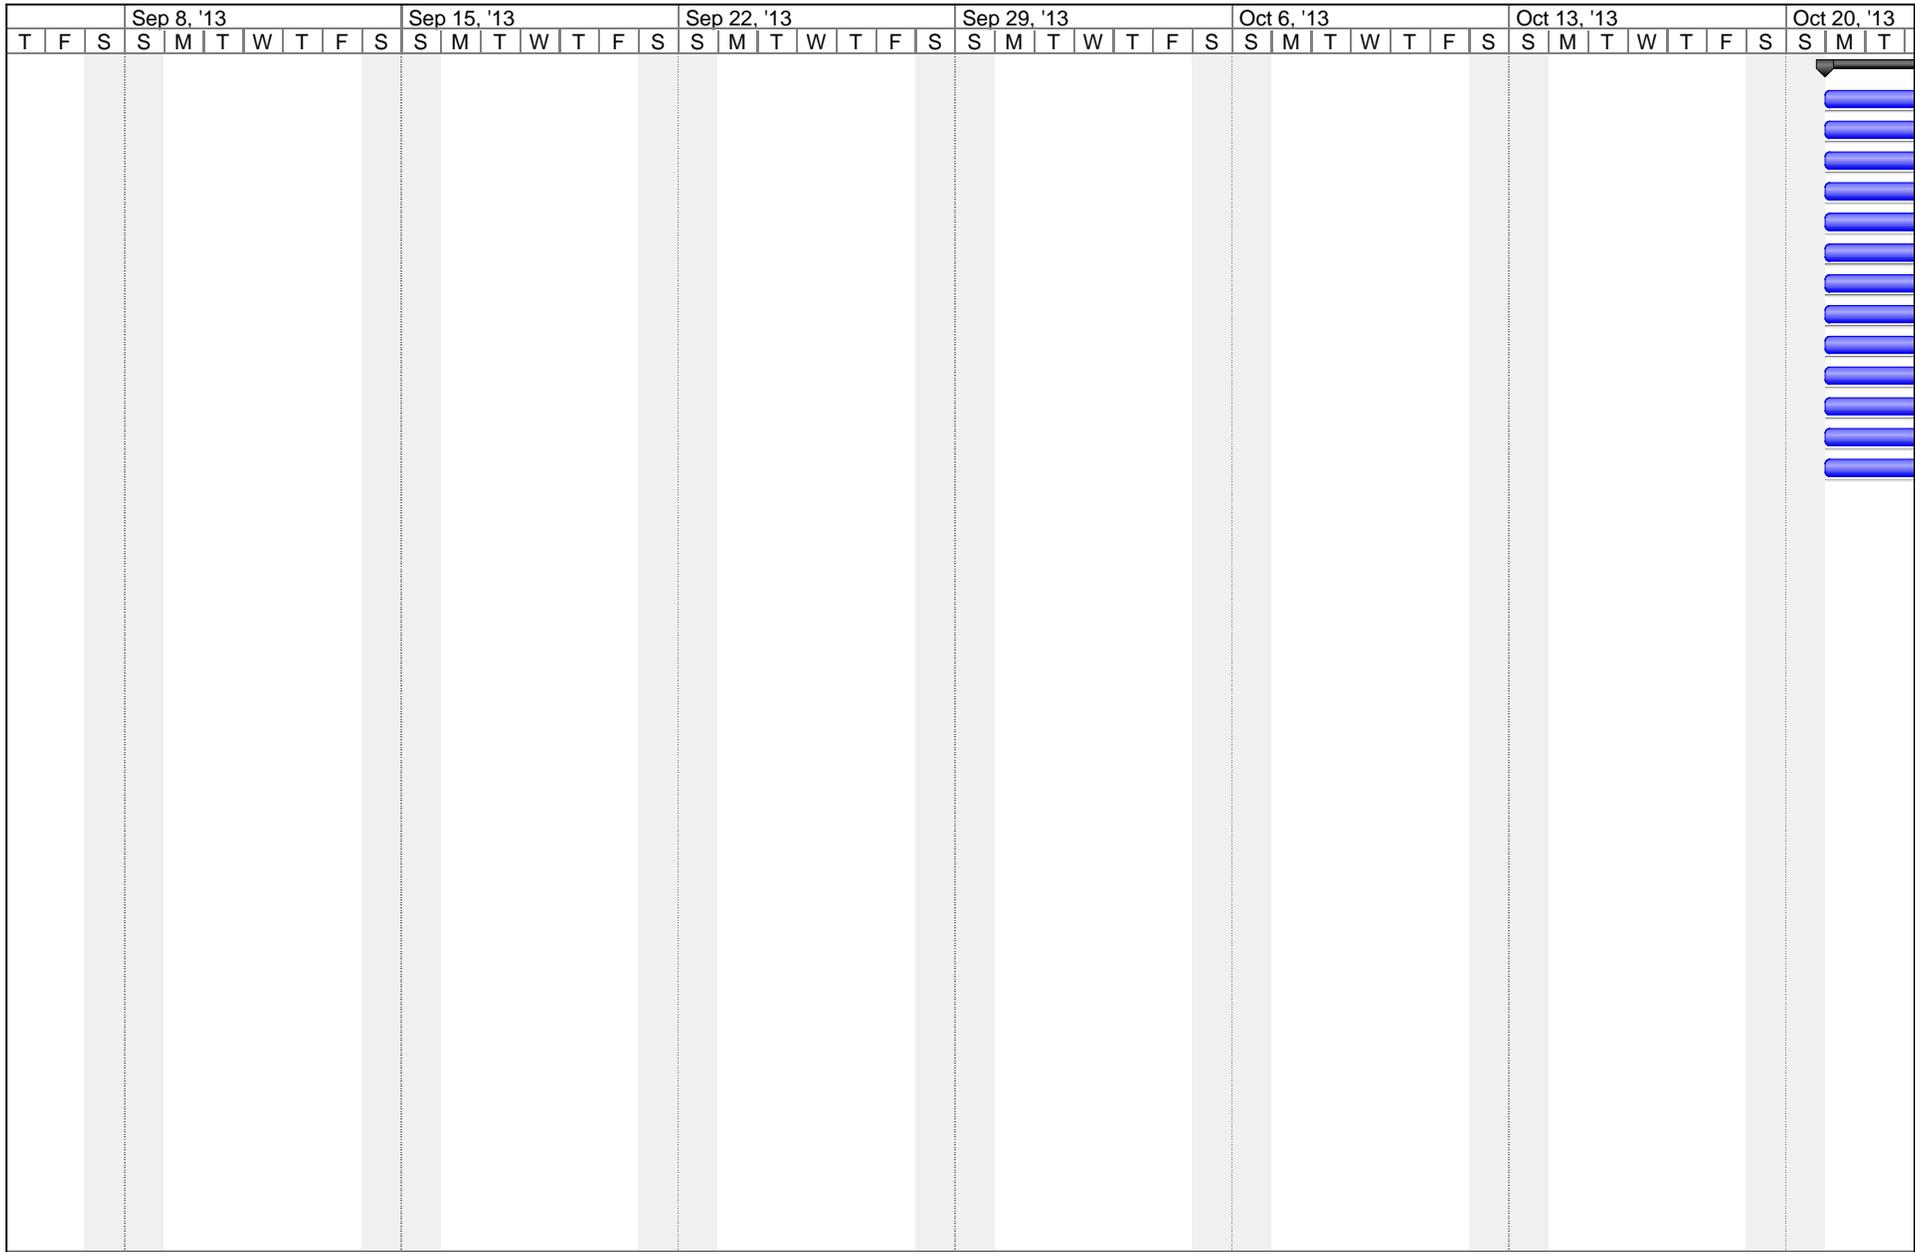

Project: LMS Project schedule as of 11/6/13 Date: Wed 11/6/13	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

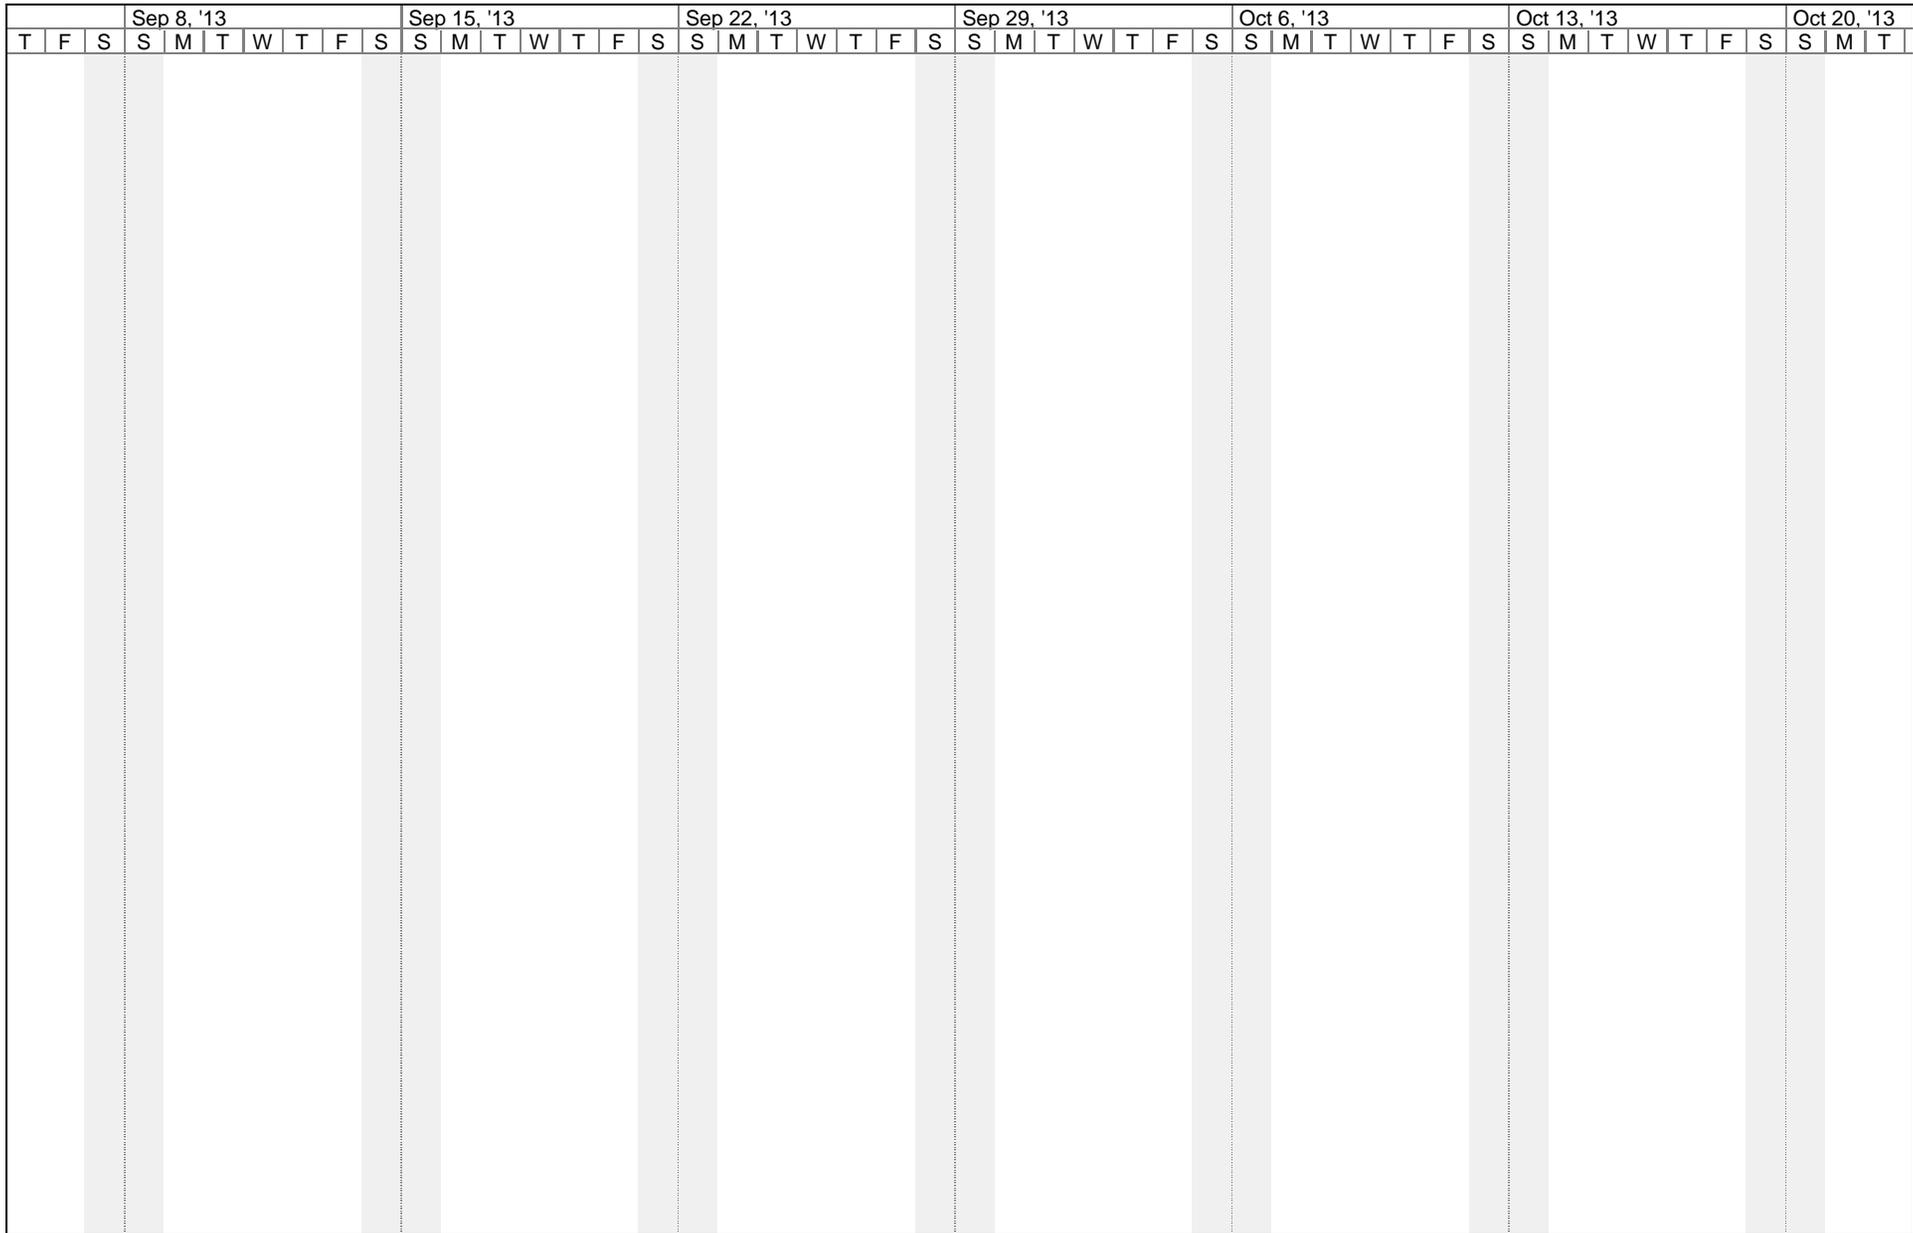


Project: LMS Project schedule as of 11/6/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

			Sep 8, '13							Sep 15, '13							Sep 22, '13							Sep 29, '13							Oct 6, '13							Oct 13, '13							Oct 20, '13		
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T




Project: LMS Project schedule as of 10/11/13 Date: Wed 11/6/13	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

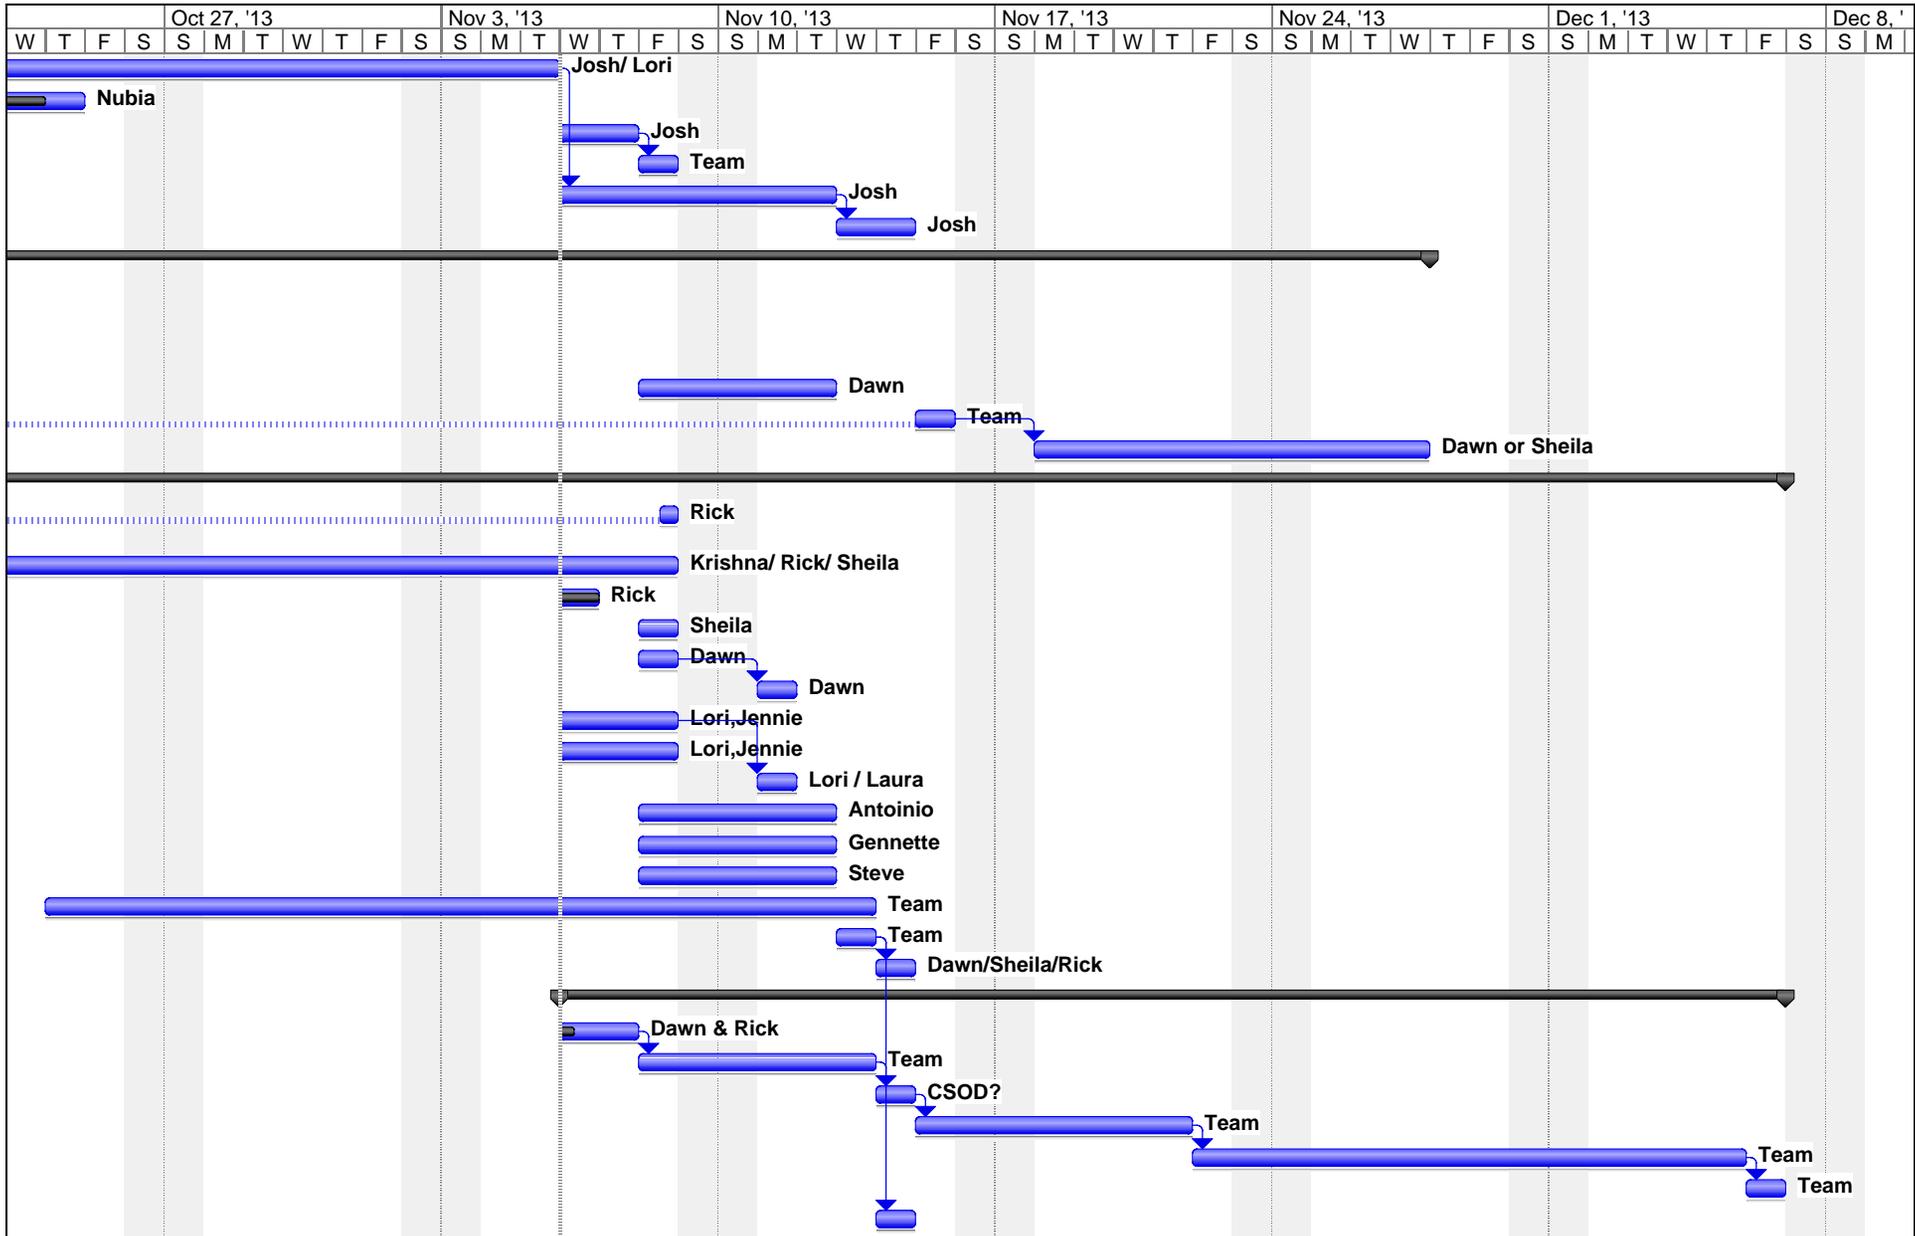


Project: LMS Project schedule as of 11/6/13
Date: Wed 11/6/13

- Task: Blue bar
- Milestone: Diamond symbol
- External Tasks: Grey bar
- Split: Dotted line
- Summary: Grey bar with arrowhead
- External Milestone: Diamond symbol
- Project Summary: Grey bar with arrowhead
- Deadline: Green arrow pointing down

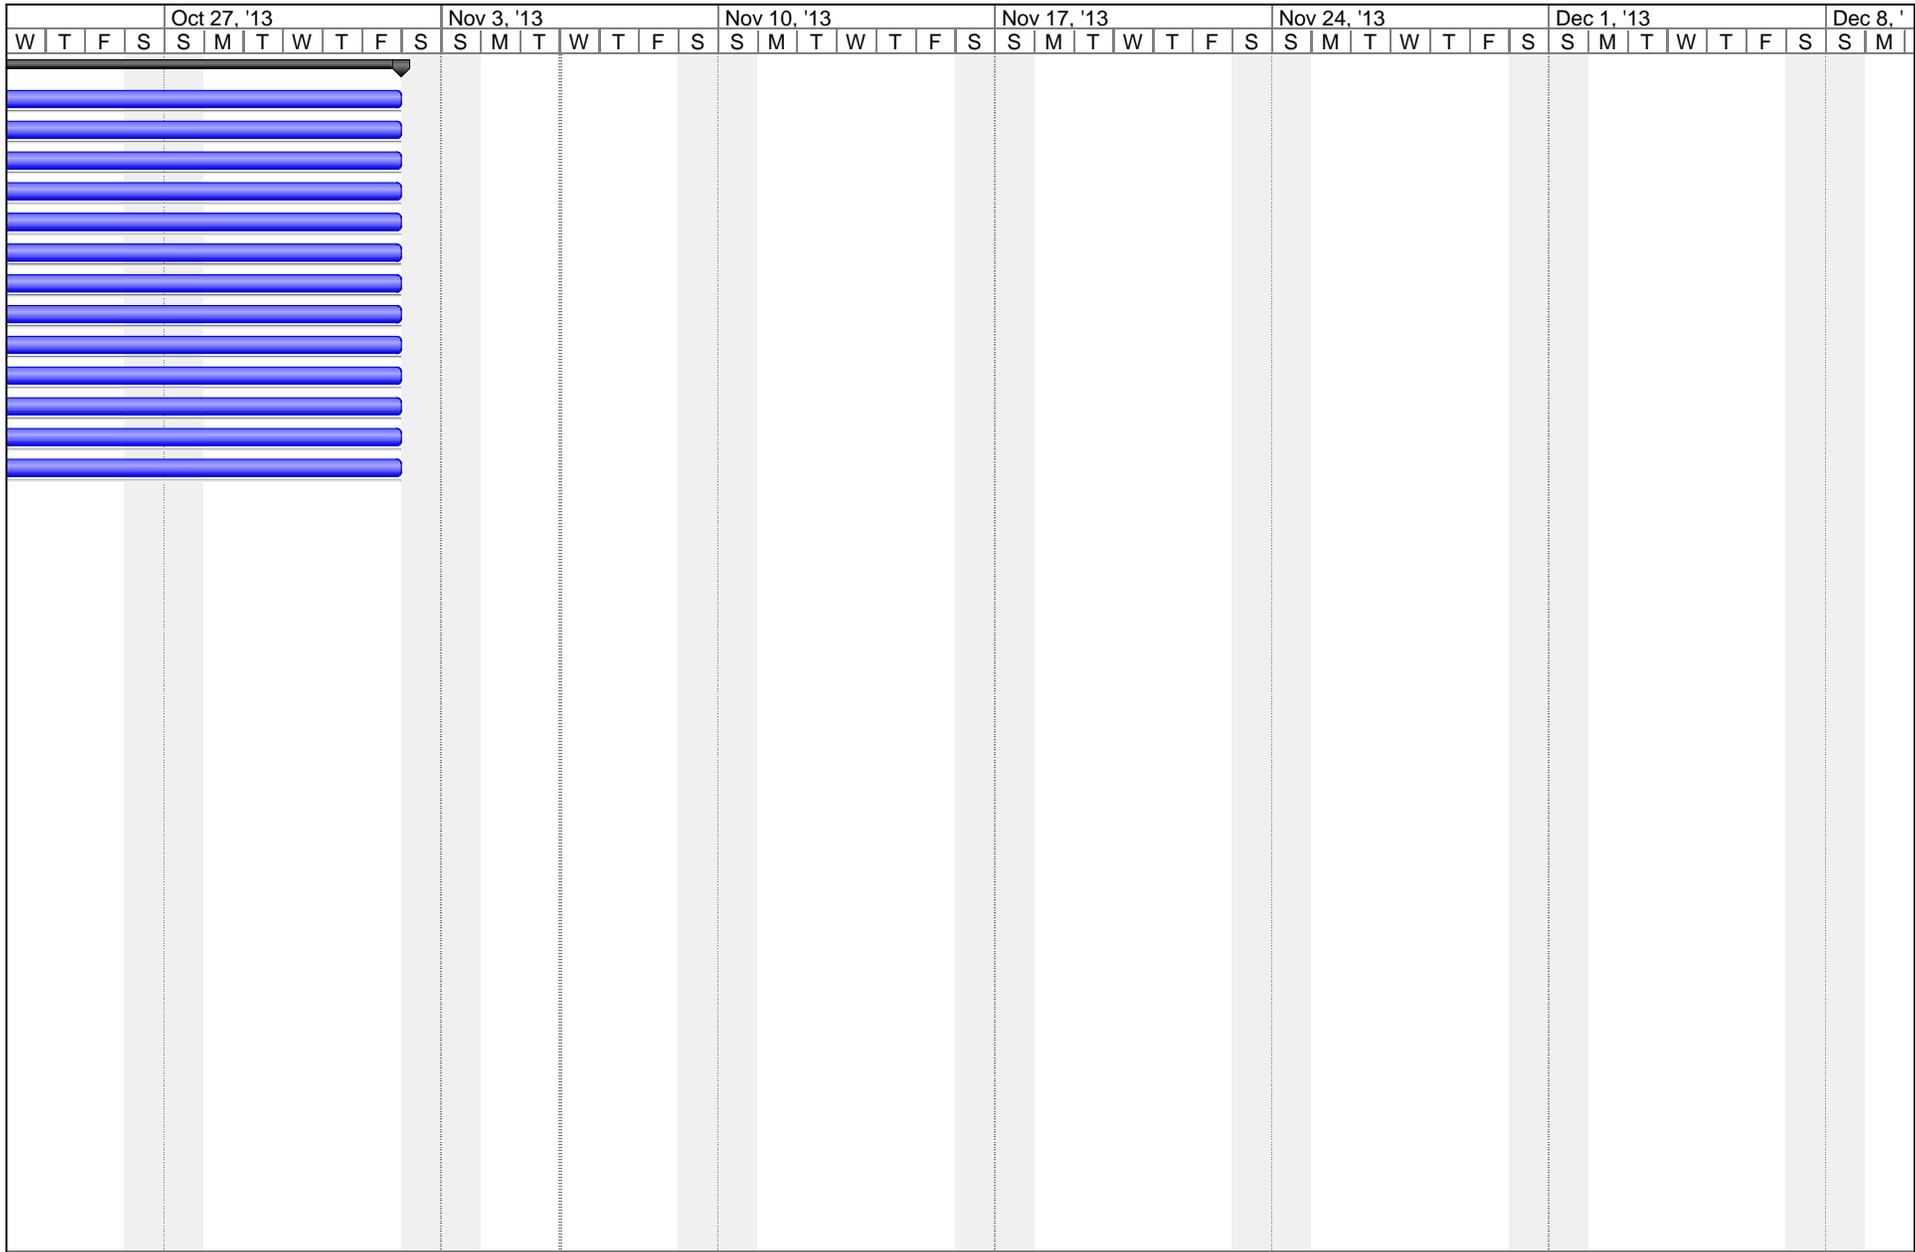

Project: LMS Project schedule as of 10/27/13 Date: Wed 11/6/13	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

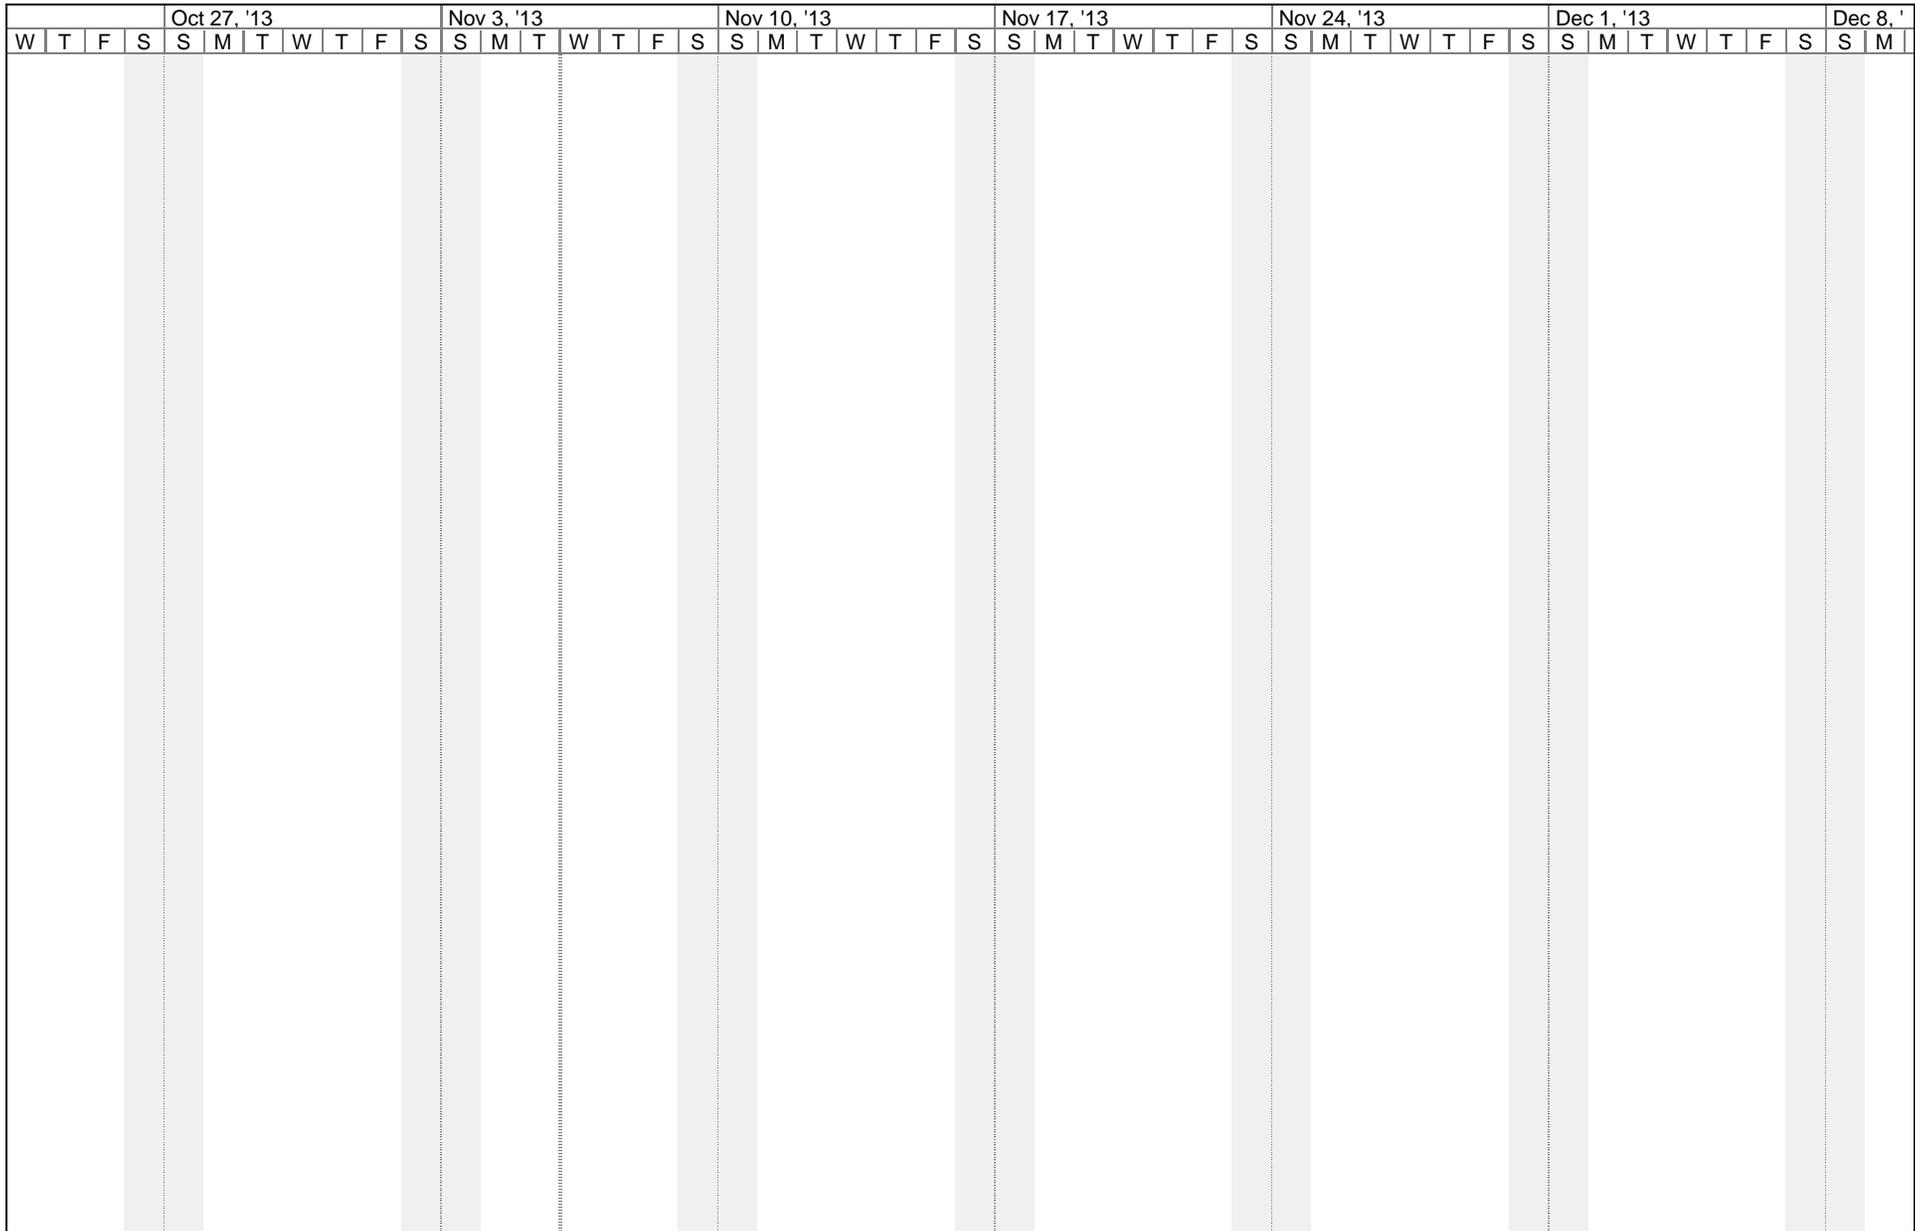

Project: LMS Project schedule as of 11/6/13
 Date: Wed 11/6/13

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

				Oct 27, '13				Nov 3, '13				Nov 10, '13				Nov 17, '13				Nov 24, '13				Dec 1, '13				Dec 8, '13												
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M



Project: LMS Project schedule as of 11/6/13 Date: Wed 11/6/13	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
